


ASMA Progress Chart 2 September 2009

* the projected completion date for main building (incl. landscape & signs) is by end sep. '09
 * the projected completion date for telescope maintenance room is by end dec. '09
 * the projected available date for move in by 2nd week of sep. '09

— contract
 — actual
 — rate

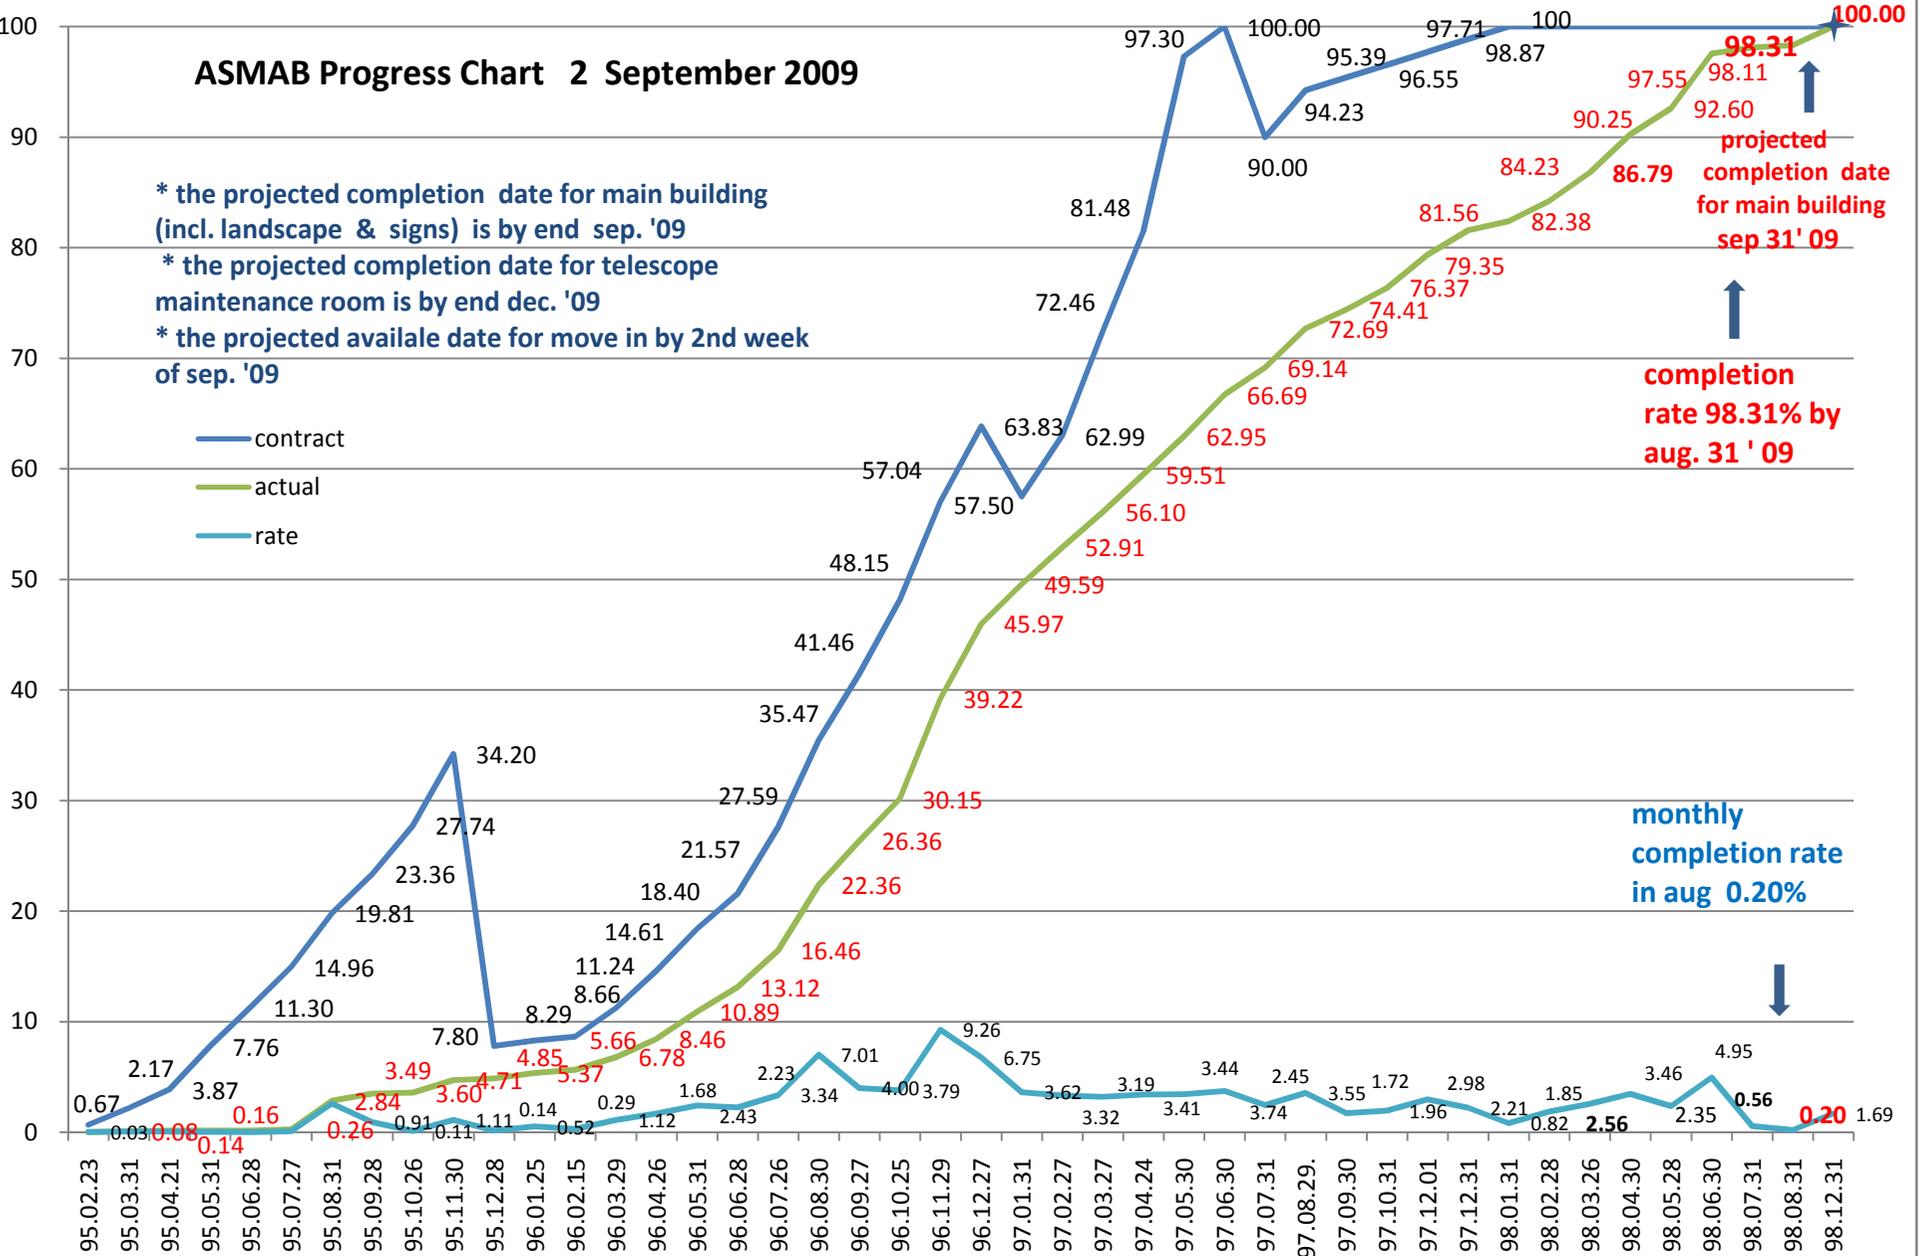

↑
 projected completion date for main building sep 31 '09

↑
 completion rate 98.31% by aug. 31 '09

monthly completion rate in aug 0.20%
